Milestone Planning

Phase Pull Planning

Lean Construction Institute
Immersive Education Program

	Mon	Tue	Wed	Thu	Fri	Mon	Tue	Wed	Thu	Fri	Mon	Tue	Wed	Thu	Fri	Mon	Tue	Wed	Thu	Fri
Swim Lanes																				

LCI Intermediate Last Planner System®

Team Name:

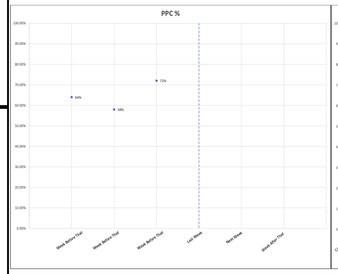

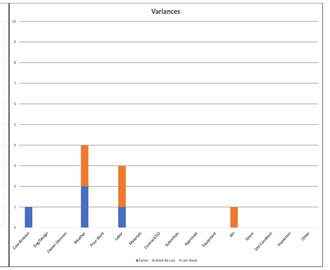

WEEKLY WORK PLAN

CATEGORIES OF PLAN FAILURE				TOTAL ACTIVITIES	
1 Coordination	5 Prerequisite Work	9 Submittals	13 Space	ACTIVITIES COMPLETED	
2 Eng/Design	6 Labor	10 Approvals	14 Site Conditions	PERCENT PLANNED COMPLETE	
3 Owner Decision	7 Materials	11 Equipment	15 Inspections		
4 Weather	8 Contracts/COs	12 RFIs	16		

Activity Description	Responsible Individual	Start Date							Done?	LEARNING	Category
Safe - Defined - Sound - Proper Sequence - Right Size - Able to Learn		Mon	Tue	Wed	Thu	Fri	Sat	Sun	Y/N	REASONS FOR PLAN FAILURE	
Workable Backlog:											

CONSTRAINT LOG

Constraining Issue	Constrained Activity/Trade	Date Identified	Date Needed	Constraint Remover (or Champion)	Promise Date	Actual Date Removed
